

Project Schedule; Gantt Chart



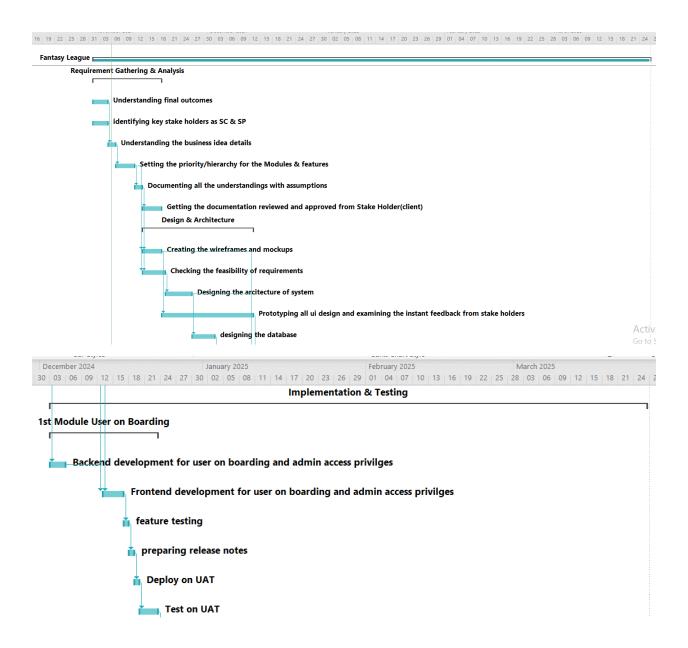

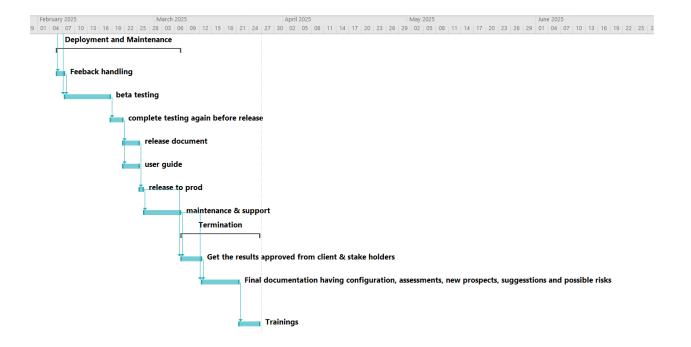

Work Breakdown Structure (WBS)

Γask Mode ■	Task Name	Duration •	Start -	Finish -	Predecessors -	Resource Names 🔻
♦	△ Fantasy League	104 days	Fri 01-11-24	Wed 26-03-25		Caffeine, Windows, Work
⇒	⁴ Requirement Gathering & Analysis	12 days	Fri 01-11-24	Mon 18-11-24		Internet, VPS, Windows, Work
♦	Understanding final outcomes	2 days	Fri 01-11-24	Mon 04-11-24		Huzaifa Shahid, Sohail Pervaiz,Ahm
♦	identifying key stake holders as SC & SP	2 days	Fri 01-11-24	Mon 04-11-24		Huzaifa Shahid, Sohail Pervaiz
♦	Understanding the business idea details	2 days	Tue 05-11-24	Wed 06-11-24	3,4	Huzaifa Shahid, Sohail Pervaiz
♦	Setting the priority/hierarchy for the Modules & features	3 days	Thu 07-11-24	Mon 11-11-24	5	Huzaifa Shahid, Sohail Pervaiz,Ahm
♦	Documenting all the understandings with assumptions	2 days	Tue 12-11-24	Wed 13-11-24	6	Huzaifa Shahid, Sohail Pervaiz,MS
♦	Getting the documentation reviewed and approved from Stake Holder(client)	3 days	Thu 14-11-24	Mon 18-11-24	7	Huzaifa Shahid, Sohail Pervaiz,MS
\rightarrow	△ Design & Architecture	21 days	Thu 14-11-24	Thu 12-12-24		
?	Creating the wireframes and mockups	3 days	Thu 14-11-24	Mon 18-11-24	6,7	Danish Gul, Huzaifa Shahid,Figi
♦	Checking the feasibility of requirements	4 days	Thu 14-11-24	Tue 19-11-24	6,7	Ahmer Noel, Huzaifa Shahid,Mu
?	Designing the arcitecture of system	5 days	Wed 20-11-24	Tue 26-11-24	11	Muhammad Ali Hassan
>	Prototyping all ui design and examining the instant feedback from stake holders	18 days	Tue 19-11-24	Thu 12-12-24	10	Danish Gul, Huzaifa Shahid,Figi
?	designing the database	4 days	Wed 27-11-24	Mon 02-12-24	12	Muhammad Ali Hassan
				-		

Mode ▼	Task Name	Duration -	Start -	Finish 🔻	Predecessors •	Resource Names 🕶
\rightarrow	4 Implementation & Testing	81.5 days	Tue 03-12-24	Wed 26-03-25		
\rightarrow	△ 1st Module User on Boarding	14.5 days	Tue 03-12-24	Mon 23-12-24		
	Backend development for user on boarding and admin access privilges	3 days	Tue 03-12-24	Thu 05-12-24	14	Muhammad Ali Hassan
	Frontend development for user on boarding and admin access privilges	2 days	Fri 13-12-24	Mon 16-12-24	10,12,13,17	Sana Mir
☆	feature testing	1 day	Tue 17-12-24	Tue 17-12-24	18	Ahmer Noel
☆	preparing release notes	1 day	Wed 18-12-24	Wed 18-12-24	19	Ahmer Noel, Sohail Pervaiz,MS
*	Deploy on UAT	1 day	Thu 19-12-24	Thu 19-12-24	20	Muhammad Ali Hassan
*	Test on UAT	1.5 days	Fri 20-12-24	Mon 23-12-24	21	Ahmer Noel, Huzaifa Shahid,Azu
\Rightarrow	⁴ 2nd Module Team Creation & Maintenance and Fantasy Gameplay	15 days	Mon 23-12-24	Mon 13-01-25		
*	feedback review of 1st Module	2 days	Mon 23-12-24	Wed 25-12-24	22	Huzaifa Shahid, MS Word,MS
*	3rd party APIs engagement to ensure RSS based model	4 days	Wed 25-12-24	Tue 31-12-24	24	Muhammad Ali Hassan
*	Backend development for fantasy team creation and maintenance including team creation, editting & deleting	4 days	Wed 25-12-24	Tue 31-12-24	24	Muhammad Ali Hassan
*	Frontend development and integration for fantasy team creation and maintenance	3 days	Tue 31-12-24	Fri 03-01-25	26	Sana Mir

Task Mode ▼	Task Name	Duration -	Start -	Finish -	Predecessors -	Resource Names
ø	user level RSS based gameplay backend development & 3rd party api integration	3 days	Tue 31-12-24	Fri 03-01-25	25	Muhammad Ali Hassan
A	user level gameplay frontend development and integration	2 days	Fri 03-01-25	Tue 07-01-25	28	Sana Mir
☆	testing features	2 days	Fri 03-01-25	Tue 07-01-25	26,28	Ahmer Noel, Sana Mir
ø	preparing release notes	2 days	Tue 07-01-25	Thu 09-01-25	30	Huzaifa Shahid, Sohail Pervaiz,MS
ø	deploy on UAT	1 day	Thu 09-01-25	Fri 10-01-25	31	Huzaifa Shahid, Muhammad Ali
×	testing on UAT	1 day	Fri 10-01-25	Mon 13-01-25	32	Ahmer Noel,VPS
\Rightarrow	4 3rd Module Leaderboard & Rewards ■ 3rd Module Leaderboard & Rewards	17 days	Mon 13-01-25	Wed 05-02-25		
☆	feedback review for 3rd Module	3 days	Mon 13-01-25	Thu 16-01-25	33	Huzaifa Shahid, MS project,MS
ø	backend development for leaderboard and rewards	3 days	Thu 16-01-25	Tue 21-01-25	35	Muhammad Ali Hassan
ø	frontend development & integration for leaderboard & reward	3 days	Tue 21-01-25	Fri 24-01-25	36	Sana Mir
¢	feature testing	2 days	Fri 24-01-25	Tue 28-01-25	37	Ahmer Noel
ø	regression & integration testing	2 days	Tue 28-01-25	Thu 30-01-25	37,38	Ahmer Noel, Azure Devops,VP
ø	release notes preparation	2 days	Thu 30-01-25	Mon 03-02-25	39	Huzaifa Shahid, MS Word,Sohail
ø	Deploy at UAT	1 day	Mon 03-02-25	Tue 04-02-25	40	Azure Devops, Muhammad Ali

Task Mode ▼	Task Name ▼	Duration -	Start 🔻	Finish 🔻	Predecessors •	Resource Names
<u></u>	Deployment and Maintenance	22 days	Wed 05-02-25	Fri 07-03-25		
*	Feeback handling	2 days	Wed 05-02-25	Fri 07-02-25	42	Huzaifa Shahid, MS Word
☆	beta testing	7 days	Fri 07-02-25	Tue 18-02-25	42,44	Ahmer Noel,VPS, Huzaifa Shahid
*	complete testing again before release	3 days	Tue 18-02-25	Fri 21-02-25	45	Ahmer Noel
ø	release document	2 days	Fri 21-02-25	Tue 25-02-25	46	MS project, MS Word,Sohail
☆	user guide	2 days	Fri 21-02-25	Tue 25-02-25	46	Huzaifa Shahid, MS Word,Sohail
ø	release to prod	1 day	Tue 25-02-25	Wed 26-02-25	47,48	Azure Devops, Muhammad Ali
ø	maintenance & support	7 days	Wed 26-02-25	Fri 07-03-25	49	Ahmer Noel, Huzaifa Shahid,M
□	4 Termination	13 days	Fri 07-03-25	Wed 26-03-25		
*	Get the results approved from client & stake holders	3 days	Fri 07-03-25	Wed 12-03-25	49,50	Huzaifa Shahid, MS project,MS
ø	Final documentation having configuration, assessments, new prospects, suggesstions and possible risks	7 days	Wed 12-03-25	Fri 21-03-25	50,52	Huzaifa Shahid, MS Word, Sohail Pervaiz
ø	Trainings	3 days	Fri 21-03-25	Wed 26-03-25	53	Huzaifa Shahid, MS Word

Resource List

Sohail Pervaiz V		HS	Managem	100%	\$35.00/hr	\$35.00/hr	\$0.00	Prorated	Standard	Project Manager and Scrum Master
	Work	SP	Document	100%	\$10.00/hr	\$10.00/hr	\$0.00	Prorated	Standard	Technical/Non technical documentation writer
Sana Mir V	Work	SM	Front end	100%	\$20.00/hr	\$20.00/hr	\$0.00	Prorated	Standard	Frontend Engineer
Muhammad Ali V Hassan	Work	MA	backend & devops	100%	\$30.00/hr	\$30.00/hr	\$0.00	Prorated	Standard	Multi Stack Critical Services Engineer
Ahmer Noel V	Work	AN	Testing	100%	\$15.00/hr	\$10.00/hr	\$0.00	Prorated	Standard	QA Engineer
Danish Gul V	Work	DG	ui/ux devel	100%	\$20.00/hr	\$20.00/hr	\$0.00	Prorated	Standard	Ui/UX Engineer
Work station N	Material	W	Equipment		\$0.00		\$0.00	Prorated		Development and Testing Machines
nternet N	Material	I	cloud		\$0.00		\$0.00	Prorated		Internet Connectivity
VPS N	Material	V	cloud		\$0.00		\$0.00	Prorated		Virtual private Servers for UAT and Production
Azure Devops C	Cost	Α	cloud					Prorated		Pipeline Management for deployment and ticket generation and working
MS project C	Cost	M	cloud					Prorated		Project Managemet and tracking tool
MS Word C	Cost	M	cloud					Prorated		Tool for documentation
igma C	Cost	F	cloud					Prorated		For creating ui/ux design, mock ups, prototypes and wireframes
Windows C	Cost	W	cloud					Prorated		Operating system which will be used to work upon
Work Place C	Cost	W	office					Prorated		A property where team will unite and sit together to build the project
Caffeine C	Cost	С	office					Prorated		An energy booster to enhance team's productivity
Brd party APIs C	Cost	3	cloud					Prorated		for RSS based feed, paid 3rd party APIs to access real time data of tournaments and pla

List of Work Products

S#	Work Product	Human Resource Responsible
1	Requirements Analysis and Documentation	Huzaifa& Sohail
2	Prototyping & Ui/UX Design	Danish Gul
3	Web Application Architecture	Muhammad Ali Hassan
4	Project Code	Muhammad Ali & Sana Mir
5	Web Application Test Plan	Ahmed Noel
6	Web Application Test Case Document	Ahmed Noel
7	QA Report	Ahmed Noel
8	WBS & Project Schedule	Huzaifa
9	Risk Plan	Huzaifa
10	User Manual & Related Documents	Sohail
